


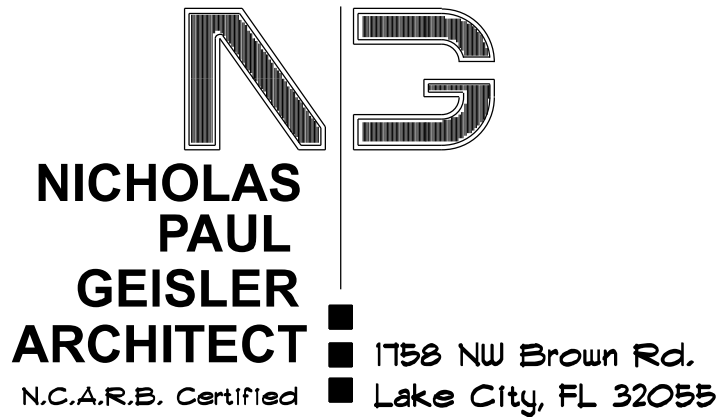

18th MAY 2021

BUILDING OFFICIAL / INSPECTOR
COUNTY BUILDING DEPT.

RE: GATOR DAVID / SPEC HOME @ MERCURY CT

TO WHOM IT MAY CONCERN:

DUE TO BEAMS NOT ATTACHING TO WALLS, 4X4 PT SYP POST WILL BE
ADDED TIGHT TO LOAD BEARING WALL. USE SIMPSON ABU44 AT BOTTOM CONNECTION
TO SLAB & SIMPSON PC44 TO BEAM. ATTACH POST TO WALL WITH (2) 5/8" X 6" LAG SCREWS
THROUGH POST TO WALL FRAMING (2 LOCATIONS @ FRONT PORCH & 2 LOCATION @ REAR PORCH)

AT FRONT PORCH BEAM TO BEAM CONNECTION, USE SIMPSON ECCLR444 TO SUPPORT BEAM.

REGARDS,

NICHOLAS PAUL GEISLER, ARCHITECT
AR0007005
