

DATE 08/31/2004

Columbia County Building Permit

PERMIT

This Permit Expires One Year From the Date of Issue

000022265

APPLICANT TERRY THRIFT PHONE 623.0115
ADDRESS 448 NW NYE HUNTER DRIVE LAKE CITY FL 32055
OWNER WILEY FEAGLE PHONE 758.9914
ADDRESS 122 SE APRIL LANE LAKE CITY FL 32025
CONTRACTOR BERNIE THRIFT PHONE 623.0046
LOCATION OF PROPERTY 441-S TO GABE RD,L, GO TO FEAGLE, L, TO APRIL,L, TO CURVE
APPROX. 3/4 MILE ON L.
TYPE DEVELOPMENT M/H & UTILITY ESTIMATED COST OF CONSTRUCTION .00
HEATED FLOOR AREA TOTAL AREA HEIGHT .00 STORIES
FOUNDATION WALLS ROOF PITCH FLOOR
LAND USE & ZONING A-3 MAX. HEIGHT
Minimum Set Back Requirments: STREET-FRONT 30.00 REAR 25.00 SIDE 25.00
NO. EX.D.U. 0 FLOOD ZONE X DEVELOPMENT PERMIT NO.

PARCEL ID 02-5S-17-09066-000 SUBDIVISION
LOT BLOCK PHASE UNIT TOTAL ACRES 110.00

IH0000075
Culvert Permit No. Culvert Waiver Contractor's License Number Applicant/Owner/Contractor
EXISTING 04-0729-E BLK RTJ N
Driveway Connection Septic Tank Number LU & Zoning checked by Approved for Issuance New Resident

COMMENTS: 1 FOOT ABOVE ROAD
AS PER RANDY TO ISSUE PERMIT.

Check # or Cash 7195/CASH

FOR BUILDING & ZONING DEPARTMENT ONLY

(footer/Slab)

Temporary Power date/app. by Foundation date/app. by Monolithic date/app. by
Under slab rough-in plumbing date/app. by Slab date/app. by Sheathing/Nailing date/app. by
Framing date/app. by Rough-in plumbing above slab and below wood floor date/app. by
Electrical rough-in date/app. by Heat & Air Duct date/app. by Peri. beam (Lintel) date/app. by
Permanent power date/app. by C.O. Final date/app. by Culvert date/app. by
M/H tie downs, blocking, electricity and plumbing date/app. by Pool date/app. by
Reconnection date/app. by Pump pole date/app. by Utility Pole date/app. by
M/H Pole date/app. by Travel Trailer date/app. by Re-roof date/app. by

BUILDING PERMIT FEE \$.00 CERTIFICATION FEE \$.00 SURCHARGE FEE \$.00
MISC. FEES \$ 200.00 ZONING CERT. FEE \$ 50.00 FIRE FEE \$ 11.34 WASTE FEE \$ 24.50
FLOOD ZONE DEVELOPMENT FEE \$ CULVERT FEE \$ TOTAL FEE 285.84
INSPECTORS OFFICE CLERKS OFFICE

NOTICE: IN ADDITION TO THE REQUIREMENTS OF THIS PERMIT, THERE MAY BE ADDITIONAL RESTRICTIONS APPLICABLE TO THIS PROPERTY THAT MAY BE FOUND IN THE PUBLIC RECORDS OF THIS COUNTY. AND THERE MAY BE ADDITIONAL PERMITS REQUIRED FROM OTHER GOVERNMENTAL ENTITIES SUCH AS WATER MANAGEMENT DISTRICTS, STATE AGENCIES, OR FEDERAL AGENCIES.

"WARNING TO OWNER: YOUR FAILURE TO RECORD A NOTICE OF COMMENCEMENT MAY RESULT IN YOUR PAYING TWICE FOR IMPROVEMENTS TO YOUR PROPERTY. IF YOU INTEND TO OBTAIN FINANCING, CONSULT WITH YOUR LENDER OR AN ATTORNEY BEFORE RECORDING YOUR NOTICE OF COMMENCEMENT."

This Permit Must Be Prominently Posted on Premises During Construction

PLEASE NOTIFY THE COLUMBIA COUNTY BUILDING DEPARTMENT AT LEAST 24 HOURS IN ADVANCE OF EACH INSPECTION, IN ORDER THAT IT MAY BE MADE WITHOUT DELAY OR INCONVENIENCE, PHONE 758-1008. THIS PERMIT IS NOT VALID UNLESS THE WORK AUTHORIZED BY IT IS COMMENCED WITHIN 6 MONTHS AFTER ISSUANCE.

The Issuance of this Permit Does Not Waive Compliance by Permittee with Deed Restrictions.

DATE 07/12/2004

Columbia County Building Permit

PERMIT

This Permit Expires One Year From the Date of Issue

000022063

APPLICANT DANNY HERRING PHONE 754-6737

ADDRESS 3882 US 90 WEST LAKE CITY FL 32055

OWNER WILEY FEAGLE PHONE 758-9914

ADDRESS 122 SE APRIL LANE LAKE CITY FL 32025

CONTRACTOR WILLIAM ROYALS PHONE _____

LOCATION OF PROPERTY 441S, TL ON GABE ST., TL ON FEAGLE, TL ON APRIL STREET
TO CURVE APPRXIMATELY 3/4 MILE ON LEFT

TYPE DEVELOPMENT MH,UTILITY ESTIMATED COST OF CONSTRUCTION .00

HEATED FLOOR AREA _____ TOTAL AREA _____ HEIGHT .00 STORIES _____

FOUNDATION _____ WALLS _____ ROOF PITCH _____ FLOOR _____

LAND USE & ZONING A-3 MAX. HEIGHT _____

Minimum Set Back Requirements: STREET-FRONT 30.00 REAR 25.00 SIDE 25.00

NO. EX.D.U. 0 FLOOD ZONE X DEVELOPMENT PERMIT NO. _____

PARCEL ID 02-5S-17-09066-000 SUBDIVISION _____

LOT _____ BLOCK _____ PHASE _____ UNIT _____ TOTAL ACRES 110.00

IH0000127

Culvert Permit No. _____ Culvert Waiver _____ Contractor's License Number _____ Applicant/Owner/Contractor _____

EXISTING 04-0729-E BK RK Y

Driveway Connection _____ Septic Tank Number _____ LU & Zoning checked by _____ Approved for Issuance _____ New Resident _____

COMMENTS: ONE FOOT ABOVE THE ROAD

Check # or Cash 20897

FOR BUILDING & ZONING DEPARTMENT ONLY

(footer/Slab)

Temporary Power _____ Foundation _____ Monolithic _____
date/app. by _____ date/app. by _____ date/app. by _____

Under slab rough-in plumbing _____ Slab _____ Sheathing/Nailing _____
date/app. by _____ date/app. by _____ date/app. by _____

Framing _____ Rough-in plumbing above slab and below wood floor _____
date/app. by _____ date/app. by _____

Electrical rough-in _____ Heat & Air Duct _____ Peri. beam (Lintel) _____
date/app. by _____ date/app. by _____ date/app. by _____

Permanent power _____ C.O. Final _____ Culvert _____
date/app. by _____ date/app. by _____ date/app. by _____

M/H tie downs, blocking, electricity and plumbing _____ Pool _____
date/app. by _____ date/app. by _____

Reconnection _____ Pump pole _____ Utility Pole _____
date/app. by _____ date/app. by _____ date/app. by _____

M/H Pole _____ Travel Trailer _____ Re-roof _____
date/app. by _____ date/app. by _____ date/app. by _____

BUILDING PERMIT FEE \$.00 CERTIFICATION FEE \$.00 SURCHARGE FEE \$.00

MISC. FEES \$ 200.00 ZONING CERT. FEE \$ 50.00 FIRE FEE \$ 17.01 WASTE FEE \$ 36.75

FLOOD ZONE DEVELOPMENT FEE \$ _____ CULVERT FEE \$ _____ TOTAL FEE 303.76

PERMIT APPLICATION / MANUFACTURED HOME INSTALLATION APPLICATION

For Office Use Only		Zoning Official <u>BLK 9/1/04</u>	Building Official <u>NO 8-24-04</u>
AP# <u>0408-73</u>	Date Received <u>8/23/04</u>	By <u>G</u>	Permit # <u>22265</u>
Flood Zone _____	Development Permit _____	Zoning _____	Land Use Plan Map Category _____
Comments _____			
<input checked="" type="checkbox"/> Site Plan with Setbacks shown <input checked="" type="checkbox"/> Environmental Health Signed Site Plan <input type="checkbox"/> Env. Health Release <input type="checkbox"/> Need a Culvert Permit <input type="checkbox"/> Need a Waiver Permit <input type="checkbox"/> Well letter provided <input checked="" type="checkbox"/> Existing Well			

- Property ID 02-55-17-09066-000 Must have a copy of the property deed
- New Mobile Home X Used Mobile Home _____ Year _____
- Subdivision Information N/A
- Applicant Chris Williams Phone # 755-8885
752-3743
- Address _____
- Name of Property Owner Wiley Feagle Geraldine Feagle Phone# 758-9914
- 911 Address 122 SE April Lane
- Name of Owner of Mobile Home Same Phone # _____
- Address Same
- Relationship to Property Owner Grandson
- Current Number of Dwellings on Property 1
- Lot Size _____ Total Acreage 110 Acres
- Explain the current driveway Existing
- Driving Directions 441 S, TL Gabe, TL on Feagle, TL on April St, to curve, (on left approximately 3/4 mile on left)
- Is this Mobile Home Replacing an Existing Mobile Home No (Assessments pd)
- Name of Licensed Dealer/Installer Bernie Thrift Phone # 623-0046
- Installers Address 212 NW Nye Hunter Dr. 2.C. 32055
- License Number IH 0000075 Installation Decal # 222612

PERMIT NUMBER

Feagle
PERMIT WORKSHEET

page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psi
or check here to declare 1000 lb. soil without testing.

X 2500 X 2500 X 2000

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 8 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X 2500 X 2000 X 2000

TORQUE PROBE TEST

The results of the torque probe test is 290 inch pounds or check here if you are declaring 5 anchors without testing. A test showing 275 inch pounds or less will require 4 foot anchors.

Note: A slate approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb holding capacity.

BDT Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Date Tested

Bernie H. B.
8-20-04

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 5

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 5

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 6

Site Preparation

Debris and organic material removed ☒

Water drainage: Natural ☒

Swale ☐

Pad ☐

Other ☐

Fastening multi wide units

Floor: Type Fastener: W Length: 30 Spacing: 12"
Walls: Type Fastener: W Length: 30 Spacing: 12"
Roof: Type Fastener: W Length: 30 Spacing: 12"
For used homes 6/11th, 30 gauge, 6" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

Type gasket NA

Installed:

Between Floors Yes NA
Between Walls Yes NA
Bottom of ridgebeam Yes NA

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 5
Siding on units is installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒

Miscellaneous

Skirting to be installed. Yes ☒ No ☐
Dryer vent installed outside of skirting. Yes ☒ No ☐
Range downflow vent installed outside of skirting. Yes ☒ No ☐
Drain lines supported at 4 foot intervals. Yes ☒ No ☐
Electrical crossovers protected. Yes ☒ No ☐
Other: NA

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature

Bernie H. B.

Date

8-20-04

PERMIT NUMBER

Installer

Bernie Thiel

License #

TH 0000075

Feag 12
CENTIMIL WORKSHEET

Address of home
being installed

Manufacturer

Destiny

Length x width

16' x 70'


NOTE:

If home is a single wide fit out one half of the blocking plan
if home is a triple or quad wide sketch in remainder of home


I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in.

Installer's initials


BVT



Show locations of Longitudinal and Lateral Systems
(use dark lines to show these locations)

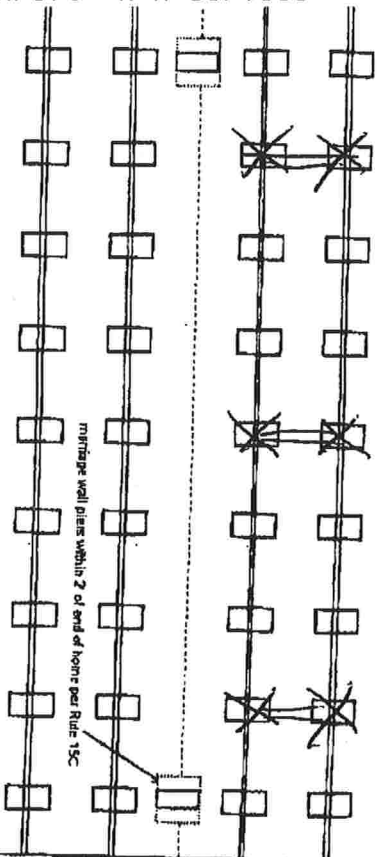

marriage wall piers within 2' of end of home per Rule 15C



New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual
Home is installed in accordance with Rule 15-C

Single wide ☒ Double wide ☐ Triple/Quad ☐

Wind Zone II ☒ Wind Zone III ☐

Installation Detail # 222612

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	16' x 16' (256)	18 1/2' x 18 1/2' (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4' 6"	6'	7'	8'	9'	10'
2000 psf	6'	8'	9'	10'	11'	12'
2500 psf	7' 6"	9'	10'	11'	12'	13'
3000 psf	8'	10'	11'	12'	13'	14'
3500 psf	8'	10'	11'	12'	13'	14'

Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 17" x 22"
Perimeter pier pad size 16" x 16"
Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening

Pier pad size



TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer

POPULAR PAD SIZES

Pad Size	Sq ft
15 x 15	225
16 x 16	256
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft 5 ft

FRAME TIES


within 2' of end of home spaced at 5' 4" oc

OTHER TIES

Number
Sidewall 32
Longitudinal 174
Marriage wall 2
Shearwall

Feasible

No. 9071 P. 2

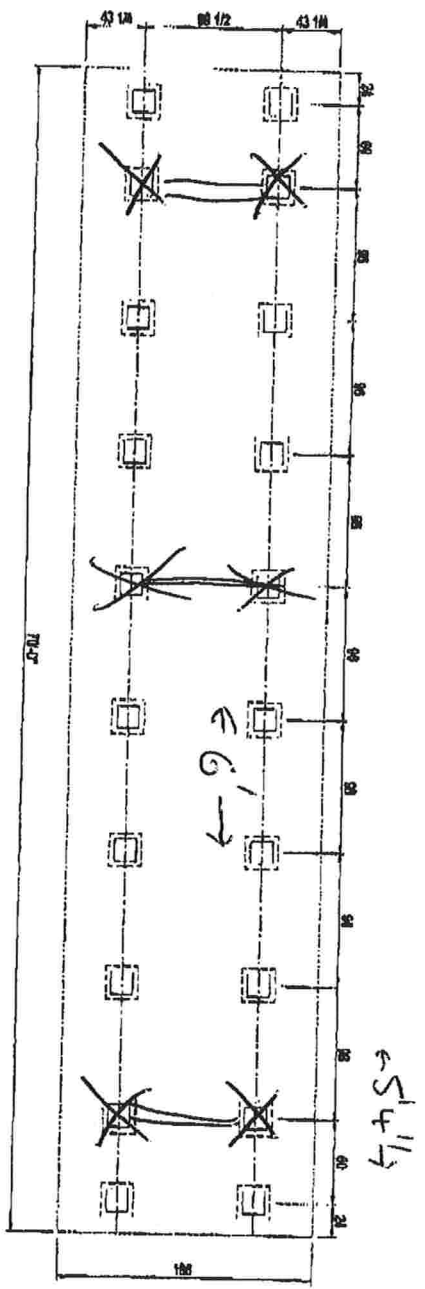

AUG. 11. 2004-10:47AM

DESIGN & CONSTRUCTION
BRADING SERVICES DEPT.
255 E. W. BROADWAY
MOBILE, AL 36684-1100
PHONE: 1-800-762-0800

Model 1101 v Oliver Systems

REVISIONS

FOUNDATION PLAN
8-24-2004 - 2004
DUNN HALL

SCALE: 1/8" = 1'-0"
DATE: 8-4-2004
BY: 1-A17
CHECKED: 1-A17

MOBILE HOME INSTALLER AFFIDAVIT

As per Florida Statutes Section 320.8249 Mobile Home Installers License:

Any person who engages in mobile home installation shall obtain a mobile home installer's license from the Bureau of Mobile Home and Recreational Vehicle Construction of the Department of Highway Safety and Motor Vehicles pursuant to this section. Said license shall be renewed annually, and each licensee shall pay a fee of \$150.

I, Bernard Thrift, license number IH 0000075
Please Print
do hereby state that the installation of the manufactured home for 1
Feagle at _____
Applicant
911 Address
will be done under my supervision.

Bernard Thrift
Signature

Sworn to and subscribed before me this _____ day of _____,
20____.

Notary Public: _____
Signature

My Commission Expires: _____
Date
