

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 2600 psf or check here to declare 1000 lb. soil without testing.

x2000 x2000 x2000

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x2000 x2000 x2000

TORQUE PROBE TEST

The results of the torque probe test is 300 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity.

DAV7 Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Date Tested

8-10-11

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 1

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 1

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 1

Site Preparation

Debris and organic material removed ok
Water drainage: Natural ✓ Swale Pad ✓ Other

Fastening multi wide units

Floor: Type Fastener: lag Length: 21" Spacing: 24"
Walls: Type Fastener: deck Length: 2 1/2" Spacing: 6 1/2"
Roof: Type Fastener: deck Length: 2 1/2" Spacing: 6 1/2"
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

DAV7

Type gasket

Red

Installed:

Between Floors Yes

Between Walls Yes

Bottom of ridgebeam Yes

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ✓ Pg.
Siding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes

Miscellaneous

Skirting to be installed. Yes ✓ No
Dryer vent installed outside of skirting. Yes ✓ N/A
Range downflow vent installed outside of skirting. Yes N/A
Drain lines supported at 4 foot intervals. Yes
Electrical crossovers protected. Yes ✓
Other:

Installer verifies all information given with this permit worksheet is accurate and true based on the


Installer Signature

[Signature]


Date

8-10-11

SITE PLAN EXAMPLE / WORKSHEET

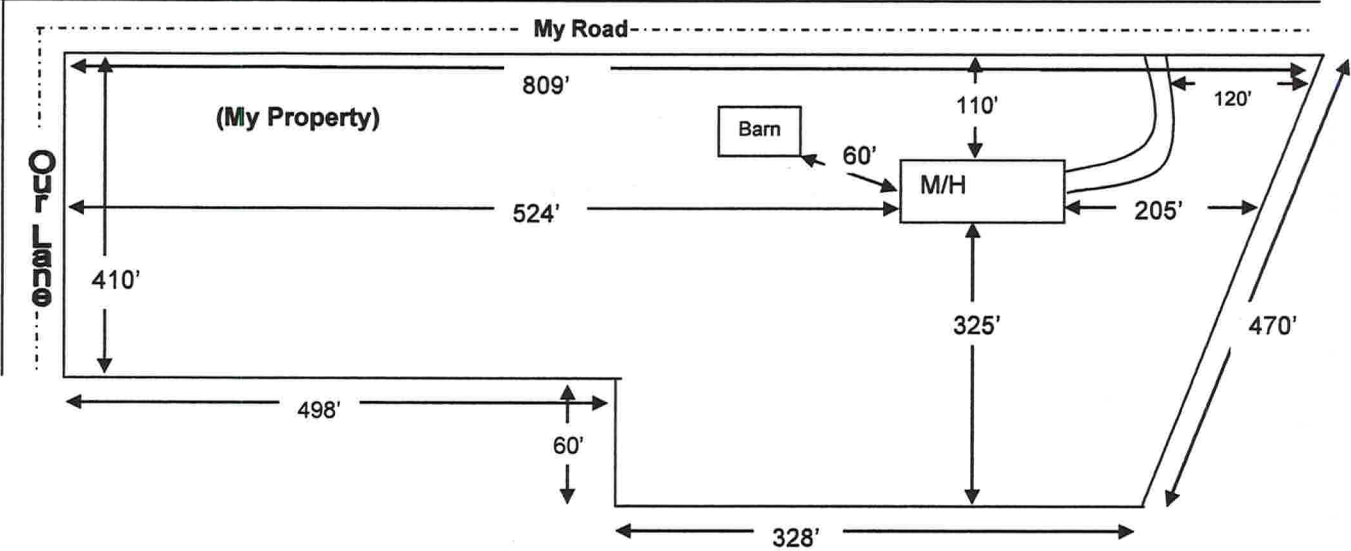


Use this example to draw your own site plan. Show all existing buildings and any other homes on this property and show the distances between them, Also show where the roads or roads are around the property. This site plan can also be used for the 911 Addressing department if you include the distance from the driveway to the nearest property line.

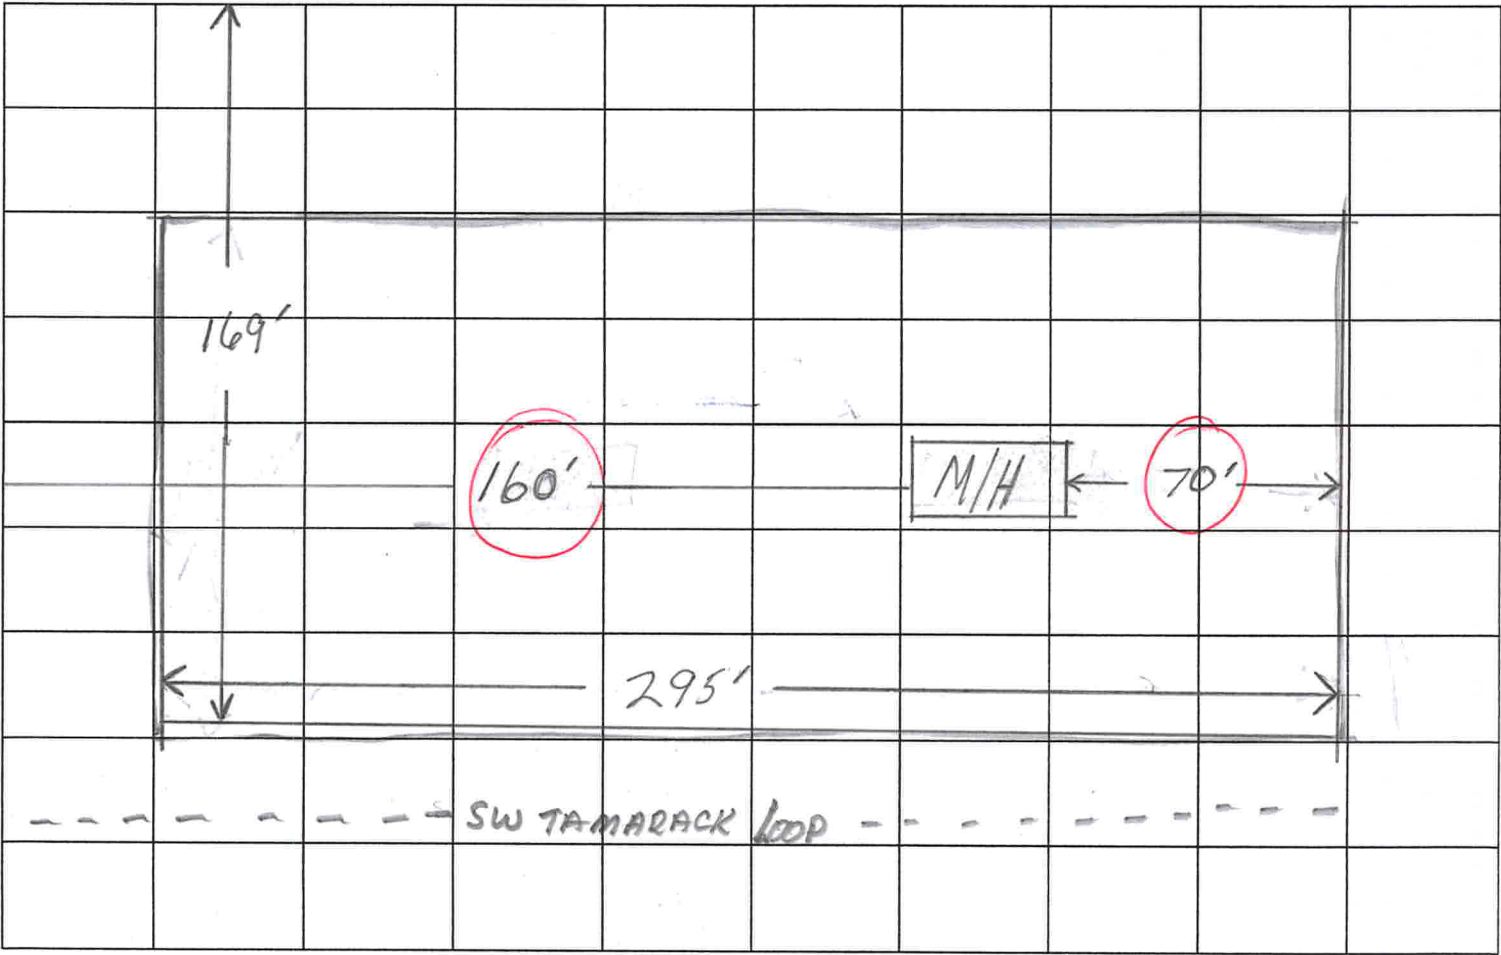


1. A PLAT, PLAN, OR DRAWING SHOWING THE PROPERTY LINES OF THE PARCEL.
2. LOCATION OF PLANNED RESIDENT OR BUSINESS STRUCTURE ON THE PROPERTY WITH DISTANCES FROM AT LEAST TWO OF THE PROPERTY LINES TO THE STRUCTURE (SEE SAMPLE BELOW).
3. LOCATION OF THE ACCESS POINT (DRIVEWAY, ETC.) ON THE ROADWAY FROM WHICH LOCATION IS TO BE ADDRESSED WITH A DISTANCE FROM A PARALLEL PROPERTY LINE AND OR PROPERTY CORNER (SEE SAMPLE BELOW).
4. TRAVEL OF THE DRIVEWAY FROM THE ACCESS POINT TO THE STRUCTURE (SEE SAMPLE BELOW).

SAMPLE:

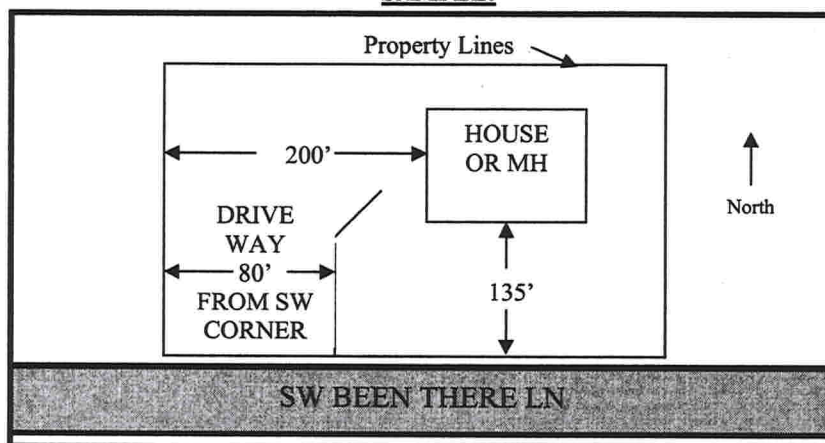

SITE PLAN BOX:

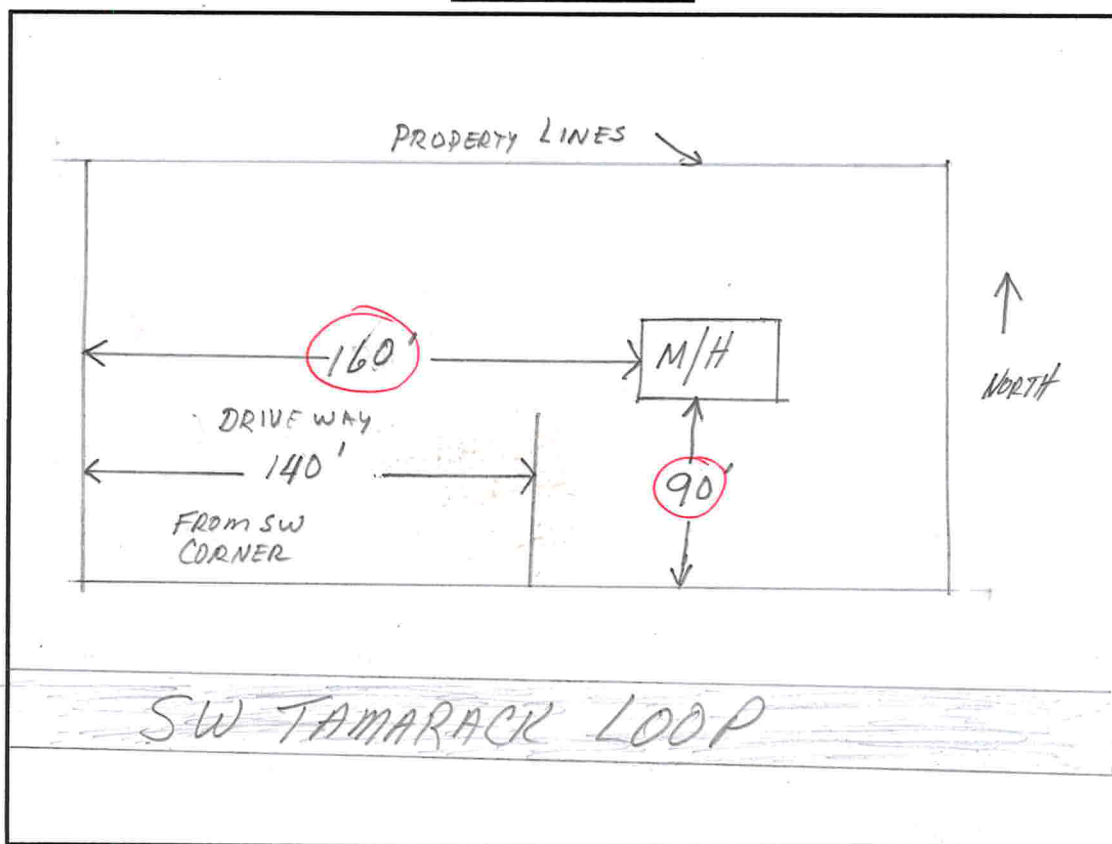

MOBILE HOME INSTALLATION SUBCONTRACTOR VERIFICATION FORM

APPLICATION NUMBER _____ CONTRACTOR _____ PHONE _____

THIS FORM MUST BE SUBMITTED PRIOR TO THE ISSUANCE OF A PERMIT

In Columbia County one permit will cover all trades doing work at the permitted site. It is REQUIRED that we have records of the subcontractors who actually did the trade specific work under the permit. Per Florida Statute 440 and Ordinance 89-6, a contractor shall require all subcontractors to provide evidence of workers' compensation or exemption, general liability insurance and a valid Certificate of Competency license in Columbia County.

Any changes, the permitted contractor is responsible for the corrected form being submitted to this office prior to the start of that subcontractor beginning any work. Violations will result in stop work orders and/or fines.

ELECTRICAL <i>OWNER</i>	Print Name _____ License #: _____	Signature _____ Phone #: _____
MECHANICAL/ <i>OWNER</i>	Print Name _____ License #: _____	Signature _____ Phone #: _____
PLUMBING/ GAS	Print Name <i>DONALD TODD</i> License #: <i>TH 102-5234</i>	Signature <i>Donald Todd</i> Phone #: <i>386-963 3433</i>

Specialty License	License Number	Sub-Contractors Printed Name	Sub-Contractors Signature
MASON			
CONCRETE FINISHER			

F. S. 440.103 Building permits; identification of minimum premium policy.--Every employer shall, as a condition to applying for and receiving a building permit, show proof and certify to the permit issuer that it has secured compensation for its employees under this chapter as provided in ss. 440.10 and 440.38, and shall be presented each time the employer applies for a building permit.

Columbia County Property

Appraiser

DB Last Updated: 6/22/2011

2010 Tax Year

Parcel: 16-4S-16-03037-001

<< Next Lower Parcel Next Higher Parcel >>

Tax Collector

Tax Estimator

Property Card

Parcel List Generator


Interactive GIS Map

Print

Owner & Property Info

Search Result: 1 of 1

Owner's Name	RICHARDS ANGELIA N &		
Mailing Address	LARRY D ROGERS 189 SW TAMARACK LP LAKE CITY, FL 32024		
Site Address	189 SW TAMARACK LOOP		
Use Desc. (code)	MOBILE HOM (000200)		
Tax District	3 (County)	Neighborhood	16416
Land Area	1.120 ACRES	Market Area	06
Description	NOTE: This description is not to be used as the Legal Description for this parcel in any legal transaction.		
COMM NE COR OF SE1/4, RUN W 290.33 FT FOR POB, CONT W 295 FT, S 169.27 FT TO N R/W OF A CO RD, E 295 FT, N 162.62 FT TO POB. ORB 899-56, 905-1871, WD 1109-476.			

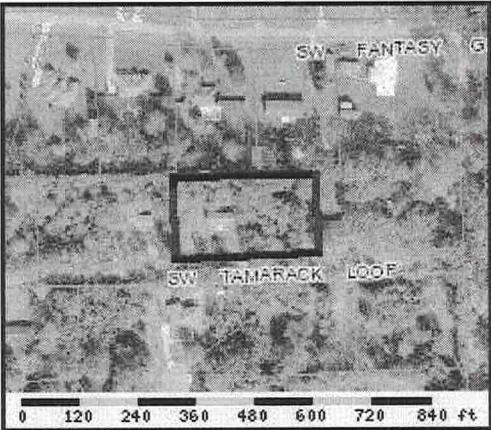

Property & Assessment Values

2010 Certified Values		
Mkt Land Value	cnt: (0)	\$18,650.00
Ag Land Value	cnt: (2)	\$0.00
Building Value	cnt: (1)	\$26,655.00
XFOB Value	cnt: (1)	\$1,200.00
Total Appraised Value		\$46,505.00
Just Value		\$46,505.00
Class Value		\$0.00
Assessed Value		\$46,505.00
Exempt Value	(code: HA)	\$23,253.00
Total Taxable Value	Cnty: \$23,252 Other: \$23,252 Schl: \$23,252	

2011 Working Values

NOTE:
2011 Working Values are NOT certified values and therefore are subject to change before being finalized for ad valorem assessment purposes.

Show Working Values

Sales History

Show Similar Sales within 1/2 mile

Sale Date	OR Book/Page	OR Code	Vacant / Improved	Qualified Sale	Sale RCode	Sale Price
1/26/2007	1109/476	WD	I	Q		\$84,000.00
6/21/2000	905/1871	WD	V	Q		\$17,500.00
3/14/2000	899/56	WD	V	U	03	\$9,000.00


Building Characteristics

Bldg Item	Bldg Desc	Year Blt	Ext. Walls	Heated S.F.	Actual S.F.	Bldg Value
1	SFR MANUF (000200)	1994	AVERAGE (05)	1344	1494	\$25,014.00
Note: All S.F. calculations are based on exterior building dimensions.						

Extra Features & Out Buildings

Code	Desc	Year Blt	Value	Units	Dims	Condition (% Good)
0190	FPLC PF	2000	\$1,200.00	0000001.000	0 x 0 x 0	(000.00)

Land Breakdown

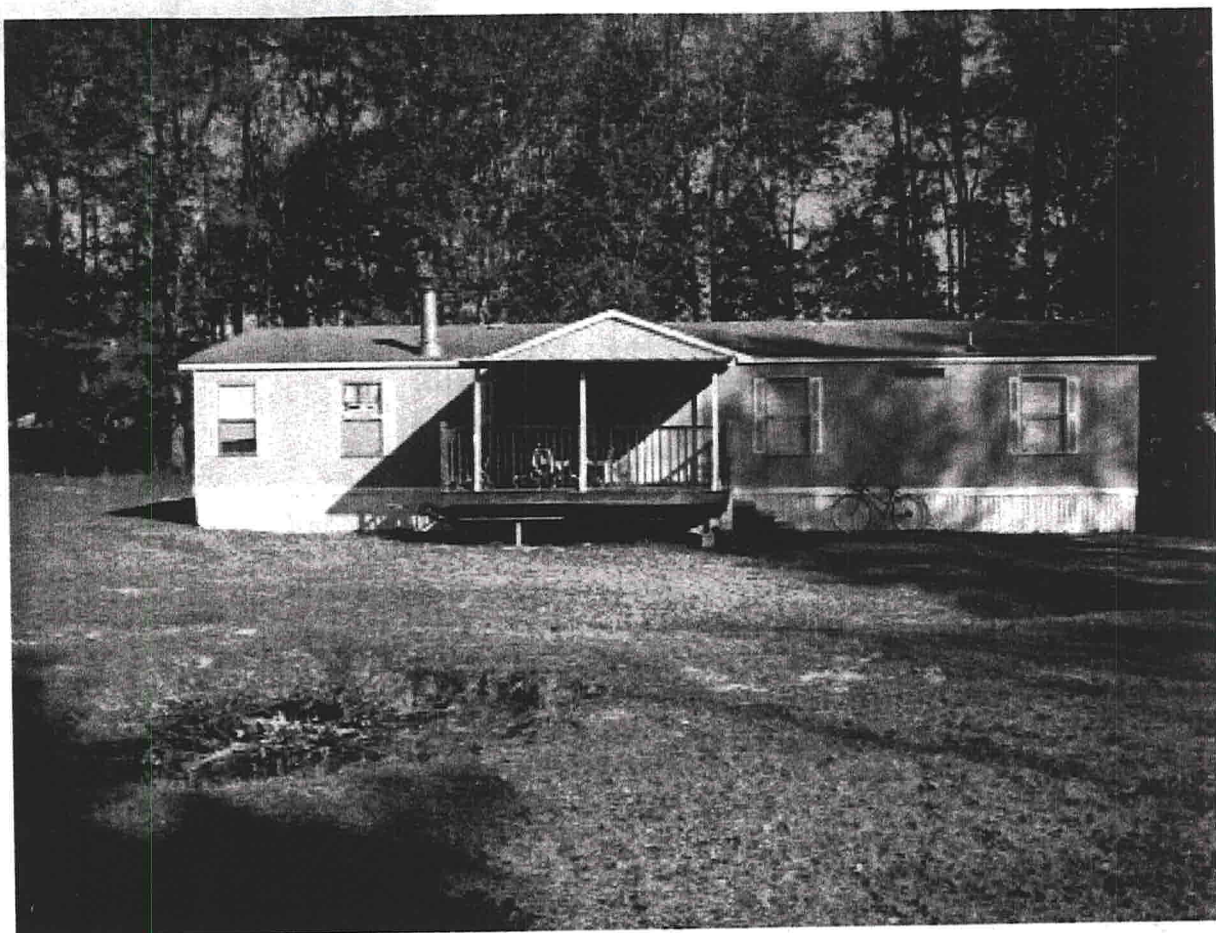

Subsidence Investigation
RICHARDS-ROGERS RESIDENCE
189 SW TAMARACK LOOP
LAKE CITY, FLORIDA
Claim Number: ACM100745

Prepared For:
AMERICAN INTEGRITY INSURANCE GROUP
TAMPA, FLORIDA

Prepared By:
SDII GLOBAL CORPORATION
SDII Project Number: 3027720

JANUARY 2011

MOBILE HOME INSTALLATION SUBCONTRACTOR VERIFICATION FORM

APPLICATION NUMBER 1108-20 CONTRACTOR Don Todd PHONE 330-4178

THIS FORM MUST BE SUBMITTED PRIOR TO THE ISSUANCE OF A PERMIT

In Columbia County one permit will cover all trades doing work at the permitted site. It is REQUIRED that we have records of the subcontractors who actually did the trade specific work under the permit. Per Florida Statute 440 and Ordinance 89-6, a contractor shall require all subcontractors to provide evidence of workers' compensation or exemption, general liability insurance and a valid Certificate of Competency license in Columbia County.

Any changes, the permitted contractor is responsible for the corrected form being submitted to this office prior to the start of that subcontractor beginning any work. Violations will result in stop work orders and/or fines.

ELECTRICAL OWNER	Print Name <u>Angelia Richards</u> License #:	Signature <u>Angelia Richards</u> Phone #:
MECHANICAL/ OWNER	Print Name <u>Angelia Richards</u> License #:	Signature <u>Angelia Richards</u> Phone #:
PLUMBING/ GAS	Print Name <u>DONALD TODD</u> License #: <u>TH 102-5234</u>	Signature <u>Donald Todd</u> Phone #: <u>386-963 3433</u>

Specialty License	License Number	Sub-Contractors Printed Name	Sub-Contractors Signature
MASON			
CONCRETE FINISHER			

F. S. 440.103 Building permits; identification of minimum premium policy.--Every employer shall, as a condition to applying for and receiving a building permit, show proof and certify to the permit issuer that it has secured compensation for its employees under this chapter as provided in ss. 440.10 and 440.38, and shall be presented each time the employer applies for a building permit.

Contractor Forms: Subcontractor form: 1/11

COLUMBIA COUNTY PERMIT WORKSHEET

page 1 of 2

These worksheets must be completed and signed by the installer.
Submit the originals with the packet.

Installer Don T. D. License # 141035234

New Home ☐ Used Home ☒
Home installed to the Manufacturer's Installation Manual ☐

911 Address where home is being installed. 189 SW Tanager Ave
Lake city FL 32024

Home is installed in accordance with Rule 15-C ☒
Single wide ☐ Wind Zone II ☒ Wind Zone III ☐
Double wide ☒ Installation Decal # 7741


Manufacturer Fleetwood Length x width 28 x 60

NOTE: if home is a single wide fill out one half of the blocking plan
if home is a triple or quad wide sketch in remainder of home

Triple/Quad ☐ Serial # AB18235H

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials DWT

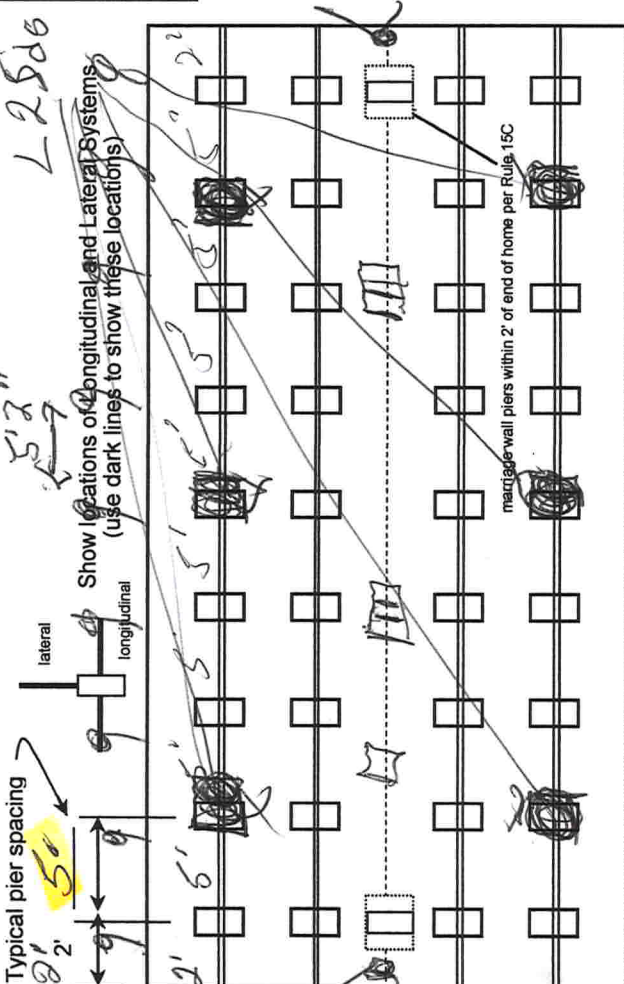

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" x 24" (576)*	26" x 26" (676)
1000 psf	3'		4'	5'	6'	7'	8'
1500 psf	4' 6"		6'	7'	8'	8'	8'
2000 psf	6'		8'	8'	8'	8'	8'
2500 psf	7' 6"		8'	8'	8'	8'	8'
3000 psf	8'		8'	8'	8'	8'	8'
3500 psf	8'		8'	8'	8'	8'	8'

* interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

I-beam pier pad size 11/2 25 1/2

Perimeter pier pad size 16 x 16

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.



List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening Pier pad size

ANCHORS

4 ft ☒ 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" oc 20

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Manufacturer SLIDE PLY

Longitudinal Stabilizing Device w/ Lateral Arms

Manufacturer

OTHER TIES

Number

Sidewall

Longitudinal

Marriage wall

Shearwall

PERMIT APPLICATION / MANUFACTURED HOME INSTALLATION APPLICATION

17123

For Office Use Only (Revised 1-11) Zoning Official BLK 11 Aug 2011 Building Official J.C. 8-11-11

AP# 1108-20 Date Received 8-10-11 By LH Permit # 29623

Flood Zone X Development Permit NIA Zoning RR Land Use Plan Map Category RES.U.L.Dem

Comments NO change - sink Hole - See Report on file

FEMA Map# NIA Elevation NIA Finished Floor 1 above RL River NIA In Floodway NIA

☒ Site Plan with Setbacks Shown ☒ EH # X11-064 ☐ EH Release ☐ Well letter ☒ Existing well

☒ Recorded Deed or Affidavit from land owner ☒ Installer Authorization ☒ State Road Access ☐ 911 Sheet 8-11-11

☐ Parent Parcel # ☐ STUP-MH ☐ F W Comp. letter ☐ VF Form Emitted on 8-11-11

IMPACT FEES: EMS ☐ Fire ☐ Corr ☐ Out County ☐ In County NOT REQUIRED

Road/Code ☐ School ☐ = TOTAL ☐ Impact Fees Suspended March 2009

Property ID # 16-45-16-03037-001 Subdivision AX-TAX#?

- New Mobile Home ☐ Used Mobile Home ☒ MH Size 60' Year 1998
- Applicant Dan Todd Phone # 386-963-3433
- Address 13021 39th Pl Willhorn FL 32094
- Name of Property Owner Angelia Richards Phone# 386-365-0422
- 911 Address 189 SW Tamarack Ln. Lake City FL 32024
- Circle the correct power company - FL Power & Light - Clay Electric
(Circle One) - Suwannee Valley Electric - Progress Energy

▪ Name of Owner of Mobile Home Same Phone #
Address

▪ Relationship to Property Owner Owner

▪ Current Number of Dwellings on Property 1

▪ Lot Size 295' x 169' Total Acreage 1.12

▪ Do you : Have Existing Drive or Private Drive or need Culvert Permit or Culvert Waiver (Circle one)
(Currently using) (Blue Road Sign) (Putting in a Culvert) (Not existing but do not need a Culvert)

▪ Is this Mobile Home Replacing an Existing Mobile Home NO

▪ Driving Directions to the Property Hwy 247 to Right on Upchurchway
Left on Tamarack 3rd house on right

- Name of Licensed Dealer/Installer Dan Todd Phone # 386-963 3433
- Installers Address 13021 39th Pl Willhorn FL 32094
 - License Number IH 1025234 Installation Decal # 7741

*330-4178

DATE 08/11/2011

Columbia County Building Permit

PERMIT

This Permit Must Be Prominently Posted on Premises During Construction

000029623

APPLICANT DON TODD PHONE 386-963-3433
ADDRESS 13021 39TH PLACE WELLBORN FL 32094
OWNER ANGELIA RICHARDS PHONE 386-365-0422
ADDRESS 189 SW TAMATAACK LOOP LAKE CITY FL 32024
CONTRACTOR DON TODD PHONE 386-330-4178
LOCATION OF PROPERTY 247 S, R UPCHURCH, L TAMARACK, 3RD ON RIGHT

TYPE DEVELOPMENT MH, UTILITY ESTIMATED COST OF CONSTRUCTION 0.00
HEATED FLOOR AREA TOTAL AREA HEIGHT STORIES
FOUNDATION WALLS ROOF PITCH FLOOR
LAND USE & ZONING RR MAX. HEIGHT 35
Minimum Set Back Requirments: STREET-FRONT 25.00 REAR 15.00 SIDE 10.00
NO. EX.D.U. 1 FLOOD ZONE X DEVELOPMENT PERMIT NO.

PARCEL ID 16-4S-16-03037-001 SUBDIVISION
LOT BLOCK PHASE UNIT TOTAL ACRES 1.12

IH1025234
Culvert Permit No. Culvert Waiver Contractor's License Number Applicant/Owner/Contractor
EXISTING X11-064 BK TC N
Driveway Connection Septic Tank Number LU & Zoning checked by Approved for Issuance New Resident

COMMENTS: FLOOR ONE FOOT ABOVE THE ROAD

NO CHARGE- SEE REPORT- SINKHOLE FORMED UNDER MH

MOVED OVER ON SAME PROPERTY Check # or Cash NO CHARGE

FOR BUILDING & ZONING DEPARTMENT ONLY

(footer/Slab)

Temporary Power date/app. by Foundation date/app. by Monolithic date/app. by
Under slab rough-in plumbing date/app. by Slab date/app. by Sheathing/Nailing date/app. by
Framing date/app. by Insulation date/app. by
Rough-in plumbing above slab and below wood floor date/app. by Electrical rough-in date/app. by
Heat & Air Duct date/app. by Peri. beam (Lintel) date/app. by Pool date/app. by
Permanent power date/app. by C.O. Final date/app. by Culvert date/app. by
Pump pole date/app. by Utility Pole date/app. by M/H tie downs, blocking, electricity and plumbing date/app. by
Reconnection date/app. by RV date/app. by Re-roof date/app. by

BUILDING PERMIT FEE \$ 0.00 CERTIFICATION FEE \$ 0.00 SURCHARGE FEE \$ 0.00
MISC. FEES \$ 0.00 ZONING CERT. FEE \$ FIRE FEE \$ 0.00 WASTE FEE \$
FLOOD DEVELOPMENT FEE \$ FLOOD ZONE FEE \$ CULVERT FEE \$ TOTAL FEE 0.00
INSPECTORS OFFICE CLERKS OFFICE

NOTICE: IN ADDITION TO THE REQUIREMENTS OF THIS PERMIT, THERE MAY BE ADDITIONAL RESTRICTIONS APPLICABLE TO THIS PROPERTY THAT MAY BE FOUND IN THE PUBLIC RECORDS OF THIS COUNTY. AND THERE MAY BE ADDITIONAL PERMITS REQUIRED FROM OTHER GOVERNMENTAL ENTITIES SUCH AS WATER MANAGEMENT DISTRICTS, STATE AGENCIES, OR FEDERAL AGENCIES.

"WARNING TO OWNER: YOUR FAILURE TO RECORD A NOTICE OF COMMENCEMENT MAY RESULT IN YOUR PAYING TWICE FOR IMPROVEMENTS TO YOUR PROPERTY. IF YOU INTEND TO OBTAIN FINANCING, CONSULT WITH YOUR LENDER OR AN ATTORNEY BEFORE RECORDING YOUR NOTICE OF COMMENCEMENT."

EVERY PERMIT ISSUED SHALL BECOME INVALID UNLESS THE WORK AUTHORIZED BY SUCH PERMIT IS COMMENCED WITHIN 180 DAYS AFTER ITS ISSUANCE, OR IF THE WORK AUTHORIZED BY SUCH PERMIT IS SUSPENDED OR ABANDONED FOR A PERIOD OF 180 DAYS AFTER THE TIME THE WORK IS COMMENCED. A VALID PERMIT RECIEVES AN APPROVED INSPECTION EVERY 180 DAYS. WORK SHALL BE CONSIDERED NOT SUSPENDED, ABANDONED OR INVALID WHEN THE PERMIT HAS RECIEVED AN APPROVED INSPECTION WITHIN 180 DAYS OT THE PREVIOUS INSPECTION.

The Issuance of this Permit Does Not Waive Compliance by Permittee with Deed Restrictions.
